

AT&T Business Migration Plan

Adobe Edge Delivery Services (EDS) Migration

Source: <https://www.business.att.com/> **Target Platform:** Adobe Edge Delivery Services (EDS) **Authoring:** Universal Editor with AEM as Content Source
Document Version: 1.0 **Date:** February 2026

Executive Summary

This document outlines the comprehensive migration plan for business.att.com to Adobe Edge Delivery Services using **Universal Editor with AEM as the content source**. This architecture combines the performance benefits of EDS delivery with enterprise-grade content management in AEM, providing visual WYSIWYG authoring while maintaining existing content governance workflows.

The migration scope includes approximately **200+ pages** across 7 product portfolios, 12 industry verticals, and supporting content sections. The site features complex interactive components including pricing configurators, product comparisons, lead generation forms, and integration with AT&T's enterprise systems.

Architecture Approach

Component	Technology	Purpose
Content Source	AEM Content Repository	Enterprise content storage, governance, workflows
Authoring	Universal Editor	Visual WYSIWYG editing experience
Delivery	Edge Delivery Services	High-performance CDN delivery, Core Web Vitals
Code Repository	GitHub	Block code, styles, scripts
Edge Functions	Edge Workers	API proxies, dynamic content, personalization

Key Benefits of UE + AEM Architecture:

- Preserves existing AEM content governance and permissions
- Visual editing with real-time preview
- Sub-second page loads via EDS global CDN
- Lighthouse scores > 90 with minimal effort
- Seamless integration with existing AT&T AEM workflows
- Edge workers for dynamic functionality (pricing, APIs)

Key Metrics

Metric	Manual Approach	With EC/AEMCoder
Total Estimated Pages	200+	200+
Product Portfolios	7	7
Industry Verticals	12	12
Individual Products	50+	50+
Custom Blocks Required	45	45
Estimated Duration	24 weeks	20-21 weeks
Total Project Hours	4,800 hours	4,120 hours
Team Size	10-12 FTEs	9-11 FTEs
Estimated Cost	\$920,000	\$790,000
Savings with EC/AEMCoder	-	~\$130,000 (14%)

Note: EC/AEMCoder automates initial block generation, reducing development effort by ~40% for block-related tasks. See Section 12 for detailed comparison.

1. Site Structure Analysis

1.1 Information Architecture

business.att.com/

- Homepage (1)
- Products/ (7 portfolios, 50+ products)
 - Cloud Connectivity/
 - Colocation
 - Content Delivery Network
 - AT&T NetBond for Cloud
 - AT&T Managed Cloud Connect
 - Cloud Connections On-Demand
 - 5G for Business/
 - Mobile 5G
 - AT&T On-Premise Edge
 - AT&T Private Cellular Networks
 - Business Internet/
 - AT&T Business Fiber
 - AT&T Dedicated Internet
 - Internet Air (Fixed Wireless)
 - DSL/IPBB
 - Cybersecurity/
 - AT&T Dynamic Defense
 - Managed Security Services
 - Threat Intelligence
 - Internet of Things/
 - IoT Platforms
 - Vehicle Solutions
 - Asset Management
 - IoT Professional Services
 - Smart Cities
 - Voice & Collaboration/
 - AT&T Office@Hand
 - AT&T IP Toll-Free
 - Business SIP Trunking
 - Cloud Voice with Microsoft Teams
 - Next Generation 9-1-1
 - Wireless/Mobility/
 - Business Unlimited Plans
 - International Add-ons
 - Field Management
 - Mobile Business Solutions
 - Enhanced Push-to-Talk
 - BYOD Solutions
 - Industries/ (12 verticals)
 - Small Business
 - Financial Services
 - Healthcare

- | — Hospitality
- | — Manufacturing
- | — Public Sector
- | — Retail
- | — Transportation
- | — Wholesale
- | — AT&T Global Business
- | — Partner Solutions
- | — FirstNet (Public Safety)
- | — Insights/ (Content Hub)
- | — Customer Stories
- | — Research Reports
- | — Tech Advice (Blog)
- | — Top Voices
- | — Support/
- | — Contact Us
- | — Premier Support
- | — Business Center Support
- | — Offers & Deals
- | — Bundles
- | — Utility Pages
- | — Sitemap
- | — Terms of Use
- | — Privacy Center
- | — Accessibility
- | — Legal Notices

1.2 Page Template Classification

Template Type	Count	Complexity	Examples
Homepage	1	Very High	Hero carousel, product tabs, CTAs, forms
Portfolio Landing	7	High	Cloud, 5G, Internet, Security, IoT, Voice, Wireless
Product Detail	50+	Medium-High	Individual product pages with specs, pricing
Industry Landing	12	Medium-High	Vertical-specific solutions
Industry Solution	20+	Medium	Sub-pages for industry features
Article/Story	30+	Medium	Customer stories, blog posts
Research Report	10+	Medium	Downloadable content with forms
Support/Contact	5	Medium	Forms, contact info, FAQs
Offers/Deals	5+	High	Dynamic pricing, promotions
Utility	10	Low	Legal, sitemap, accessibility

2. Migration Steps & Activities

Phase 0: Pre-Migration (Weeks 1-2)

Step	Activity	Owner	Hours	Deliverables
0a	Site audit & inventory	Content Strategist	40	Complete page inventory, asset list
0b	Performance baseline	Tech Lead	24	Current Core Web Vitals report
0c	SEO audit	SEO Specialist	32	Rankings, meta data, structured data
0d	Stakeholder alignment & kickoff	PM	24	RACI matrix, kickoff deck, timeline
0e	Technical discovery	Tech Lead	40	API inventory, integration mapping
	Phase 0 Total		160	

Phase 1: Foundation (Weeks 3-6)

Step	Activity	Owner	Manual Hrs	EC/AEMCoder Hrs	Deliverables
1	Run EC/AEMcoder for initial migration	Dev Team	80	40	Initial blocks, markdown, page structure
2	Update blocks, functionality, CSS	Dev Team	160	80	Production-ready block code
2a	Extract design system tokens	Dev Team	80	60	styles.css, CSS custom properties
2b	Typography & font setup	Dev Team	24	24	fonts.css, AT&T brand fonts
2c	Core navigation blocks	Dev Team	80	80	header/, footer/, mega-menu
	Phase 1 Total		424	284	

Phase 2: Content Modeling (Weeks 7-8)

Step	Activity	Owner	Hours	Deliverables
3	Create component-model.json	Tech Lead	60	JCR package structure for AEM importer
3a	Create component-definitions.json	Tech Lead	60	Universal Editor field definitions
3b	Define content fragment models	Content Strategist	40	CF models for products, stories
3c	Update transformations	Dev Team	40	Import script transformations
	Phase 2 Total		200	

Phase 3: Block Development (Weeks 9-14)

Step	Activity	Owner	Manual Hrs	EC/AEMCoder Hrs	Deliverables
4a	Hero blocks (6 variants)	Dev Team	120	72	hero-video, hero-carousel, hero-split, etc.
4b	Card blocks (10 variants)	Dev Team	200	100	cards-product, cards-feature, cards-pricing, etc.
4c	Interactive blocks	Dev Team	280	168	tabs, accordion, carousel, modal, search
4d	Form blocks	Dev Team	120	72	lead-form, contact-form, newsletter
4e	Content blocks	Dev Team	160	80	columns, quote, table, embed, download
4f	Product-specific blocks	Dev Team	200	108	pricing-table, comparison, spec-sheet
	Phase 3 Total		1,080	600	

Note: EC/AEMCoder estimates assume AI-generated block scaffolding with manual refinement for brand compliance, accessibility, and complex interactions.

Phase 4: Page Review & Asset Migration (Weeks 15-16)

Step	Activity	Owner	Hours	Deliverables
4	Review each page, re-author assets	Content Team	200	Validated content in AEM DAM
4a	Create URL redirect mapping	Content Strategist	40	301 redirect spreadsheet
4b	DAM asset migration	Content Team	80	Assets with metadata in AEM
4c	Image optimization	Dev Team	40	WebP conversion, lazy loading
	Phase 4 Total		360	

Phase 5: Edge Workers & APIs (Weeks 17-18)

Step	Activity	Owner	Hours	Deliverables
5	Move servlets/APIs to Edge workers	Dev Team	160	Edge worker functions
5a	Pricing API integration	Dev Team	60	Dynamic pricing endpoints
5b	Lead form submission handling	Dev Team	40	Form backend integration
5c	Search functionality	Dev Team	80	Site search implementation
	Phase 5 Total		340	

Phase 6: AEM Migration (Weeks 19-20)

Step	Activity	Owner	Hours	Deliverables
6	Migrate custom functionality to AEMaaCS	Dev Team	120	Reports, scheduled jobs
7	Migrate meta-schema, taxonomy, workflows	Tech Lead	80	AEM configurations
7a	User/group migration	Admin	40	Permissions in AEMaaCS
7b	Workflow configuration	Tech Lead	40	Approval workflows
	Phase 6 Total		280	

Phase 7: Integrations (Weeks 21-22)

Step	Activity	Owner	Hours	Deliverables
8a	Analytics/tracking setup	Dev Team	60	Adobe Launch configuration
8b	Third-party scripts	Dev Team	40	Chat, pixels, consent banner
8c	Search indexing configuration	Dev Team	40	Sitemap, robots.txt
8d	Social meta tags	Dev Team	20	OG tags, Twitter cards
	Phase 7 Total		160	

Phase 8: Validation & Testing (Weeks 23-24)

Step	Activity	Owner	Hours	Deliverables
8	Validate all functionalities	QA Team	160	Functional test reports
9	Accessibility audit (WCAG 2.1 AA)	QA Team	80	Accessibility report, fixes
10	Performance/load testing	QA Team	60	Performance test results
11	SEO validation	SEO Specialist	40	Redirect testing, sitemap validation
12	Security review	Security Team	40	Security headers, CSP audit
	Phase 8 Total		380	

Phase 9: Launch (Week 24+)

Step	Activity	Owner	Hours	Deliverables
13	UAT & stakeholder sign-off	PM	80	Sign-off documentation
14	DNS cutover & rollback plan	Tech Lead	40	Production deployment
15	Author training on Universal Editor	Training Lead	60	Training materials, sessions
16	Hypercare & monitoring setup	DevOps	80	Monitoring dashboards, alerts
	Phase 9 Total		260	

3. Complete Step Summary

AT&T BUSINESS EDS MIGRATION - 18 STEP PLAN

PRE-MIGRATION (160 hrs)

0a. Site audit & inventory

0b. Performance/SEO baseline

0c. SEO audit (rankings, meta data, structured data)

0d. Stakeholder alignment & kickoff

0e. Technical discovery (API inventory)

MIGRATION EXECUTION (2,344 hrs)

1. Run EC/AEMcoder for business.att.com initial migration

2. Update blocks, add functionality, fix CSS

2a. Extract design system tokens

2b. Typography & font setup

2c. Core navigation blocks (header, footer, mega-menu)

3. Create component-model.json for JCR package

3a. Create component-definitions.json for Universal Editor

3b. Define content fragment models

3c. Update import transformations

4. Review each page, re-author assets in DAM

4a. Create URL redirect mapping

4b. DAM asset migration with metadata

4c. Image optimization (WebP, lazy loading)

5. Move existing servlets/APIs to Edge workers

5a. Pricing API integration

5b. Lead form submission handling

5c. Search functionality implementation

6. Migrate custom functionality (reports, jobs) to AEMaaCS

7. Migrate meta-schema, taxonomy, workflows, users to AEMaaCS

7a. User/group permissions migration

7b. Workflow configuration

INTEGRATIONS (160 hrs)

8a. Analytics/tracking setup (Adobe Launch)

8b. Third-party scripts (chat, pixels, consent)

8c. Search indexing configuration

8d. Social meta tags (OG, Twitter cards)

VALIDATION & LAUNCH (640 hrs)

8. Validate all existing functionalities work as-is

9. Accessibility audit & fixes (WCAG 2.1 AA)

10. Performance/load testing

11. SEO validation (redirects, sitemap, robots.txt)

12. Security review (headers, CSP)

13. UAT & stakeholder sign-off

14. DNS cutover (with rollback plan)

15. Author training on Universal Editor

16. Hypercare & post-launch monitoring

MANUAL TOTAL: 3,644 base hours + contingency = 4,800 hours

EC/AEMCODER TOTAL: 2,964 base hours + contingency = 4,120 hours

APPROACH COMPARISON:

Manual: 24 weeks | 4,800 hours | \$920,000

EC/AEMCoder: 20 weeks | 4,120 hours | \$790,000

SAVINGS: 4 weeks | 680 hours | \$130,000 (14%)

4. Block Requirements

4.1 Required EDS Blocks (45 Total)

Navigation Blocks (4)

Block Name	Complexity	Notes
header	Very High	Mega menu, search, account login, Personal/Business toggle
footer	High	Multi-column, social links, legal links
breadcrumb	Low	Standard hierarchy
mobile-nav	High	Mobile menu with nested items

Hero Blocks (6)

Block Name	Complexity	Notes
hero-video	High	Background video with overlay text, CTAs
hero-carousel	High	Multiple slides with auto-rotation
hero-tabs	High	Tabbed content (Mobile, Internet, Voice, etc.)
hero-split	Medium	Two-column layout
hero-minimal	Low	Text-only section header
hero-promo	Medium	Promotional banner with pricing

Card Blocks (10)

Block Name	Complexity	Notes
cards-product	Medium	Product tiles with pricing
cards-feature	Medium	Icon/image with text
cards-pricing	High	Pricing comparison cards
cards-industry	Medium	Industry solution cards
cards-story	Medium	Customer story previews
cards-stat	Medium	Large numbers with descriptions
cards-cta	Low	Simple call-to-action cards
cards-icon	Medium	Icon-based feature cards
cards-testimonial	Medium	Customer quotes
cards-link	Low	Quick link lists

Interactive Blocks (10)

Block Name	Complexity	Notes
accordion	Medium	FAQ, product details
tabs	Medium	Content organization
carousel	High	Image/content slider
modal	Medium	Popup dialogs, offer details
video	Medium	Inline video player
video-modal	High	Lightbox video player
search	High	Site search with filtering
filter	High	Product filtering
pricing-calculator	Very High	Dynamic pricing tool
comparison-table	High	Product comparison

Content Blocks (8)

Block Name	Complexity	Notes
columns	Low	Multi-column layouts
quote	Low	Testimonials, pull quotes
table	Medium	Data tables
embed	Medium	External content (YouTube, maps)
download	Low	PDF/document links
cta-banner	Medium	Full-width call-to-action
divider	Low	Section separators
icon-list	Medium	Feature lists with icons

Form Blocks (4)

Block Name	Complexity	Notes
lead-form	High	Sales contact form (RAI form)
contact-form	Medium	General inquiry
newsletter	Medium	Email signup
search-input	Medium	Search box

AT&T-Specific Blocks (3)

Block Name	Complexity	Notes
guarantee-banner	Medium	AT&T Guarantee messaging
offer-card	High	Dynamic promotional offers
jd-power-badge	Low	Award/certification badges

4.2 Block Summary

Category	Block Count	Avg Complexity
Navigation	4	High
Hero	6	Medium-High
Cards	10	Medium
Interactive	10	High
Content	8	Low-Medium
Forms	4	Medium-High
AT&T-Specific	3	Medium
Total	45	Medium-High

5. Technical Requirements

5.1 Design System

Typography

Font	Usage	Source
AT&T Aleck Sans	Headlines, display	Custom (AT&T brand)
AT&T Aleck Slab	Accent text	Custom (AT&T brand)
System fonts	Body text	System stack fallback

Color Palette

Color	Hex	Usage
AT&T Blue	#009FDB	Primary brand, links
AT&T Dark Blue	#0568AE	Headers, CTAs
AT&T Black	#000000	Body text
AT&T Gray	#5A5A5A	Secondary text
White	#FFFFFF	Backgrounds
Light Gray	#F2F2F2	Secondary backgrounds

5.2 Integrations Required

Integration	Priority	Complexity	Notes
Adobe Analytics/Launch	Critical	Medium	Tag management, conversion tracking
ChiliPiper (Concierge)	High	Medium	Lead routing, scheduling
OneTrust	High	Medium	Cookie consent, GDPR/CCPA
Site Search	High	High	Algolia or similar
Lead Form Backend	Critical	High	CRM integration
AT&T Business Center	Medium	High	Account management links
Premier Support	Medium	Medium	Customer portal integration
Chat Widget	Medium	Low	Customer support chat

5.3 Edge Workers Required

Worker	Purpose	Complexity
pricing-api	Dynamic pricing calculation	High
lead-routing	Form submission handling	Medium
search-proxy	Search API proxy	Medium
offer-personalization	Dynamic offers based on segment	High
analytics-proxy	Server-side analytics	Low


5.4 Performance Targets

Metric	Target	Current Benchmark
LCP	< 2.5s	TBD
FID/INP	< 100ms	TBD
CLS	< 0.1	TBD
Lighthouse Score	> 90	TBD
Page Weight	< 1.5MB	TBD
Time to Interactive	< 3s	TBD


6. Timeline & Phases

6.1 Gantt Chart

AT&T BUSINESS EDS MIGRATION - PROJECT GANTT CHART (24 Weeks)

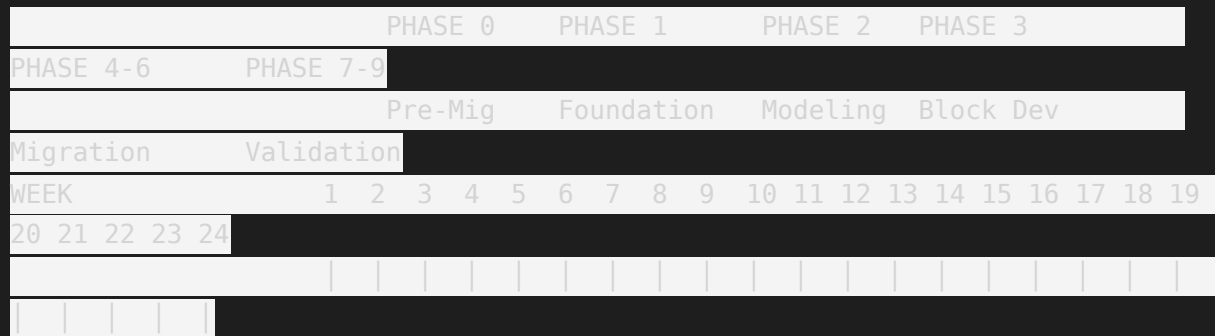

PHASE 0: PRE-MIGRATION (160 hrs)




PHASE 1: FOUNDATION (424 hrs)



PHASE 2: CONTENT MODELING (200 hrs)



PHASE 3: BLOCK DEVELOPMENT (1,080 hrs)

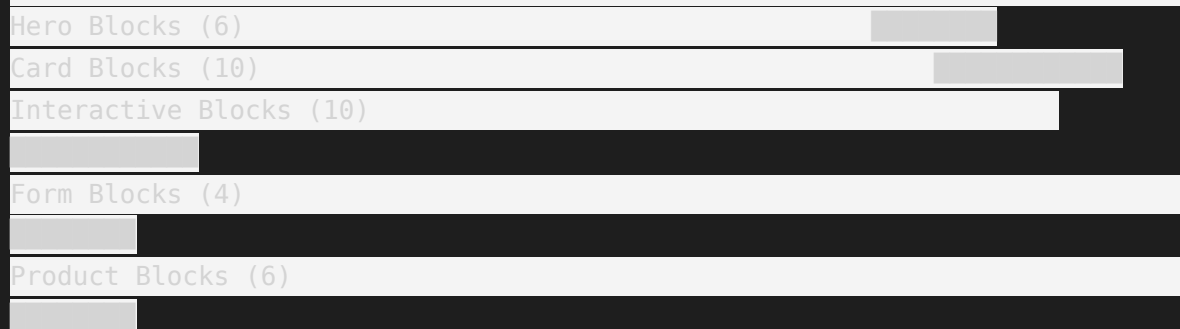

PHASE 4-6: PAGE REVIEW & MIGRATION (980 hrs)

Page Review & Assets

Edge Workers & APIs

AEM Migration

PHASE 7-9: INTEGRATIONS & LAUNCH (800 hrs)

Integrations Setup

Validation & Testing

UAT & Go-Live

MILESTONES

Kickoff		Design		Models		Blocks 50%		All Blocks	
Content	UAT	GO-LIVE							
Done		System		Done		Complete		Done	
100%									
W2		W6		W8		W12		W14	
W23		W24							

LEGEND:  = Active Work Period  = Milestone

Total: 4,800 Hours | 24 Weeks | 10-12 FTEs | ~\$920K

6.2 Phase Overview

Phase 0: Pre-Migration (Weeks 1-2) ————— 160 hours

- └─ Site audit & inventory (40 hrs)
- └─ Performance baseline (24 hrs)
- └─ SEO audit (32 hrs)
- └─ Stakeholder kickoff (24 hrs)
- └─ Technical discovery (40 hrs)

Phase 1: Foundation (Weeks 3-6) ————— 424 hours

- └─ EC/AEMcoder initial migration (80 hrs)
- └─ Block updates & CSS (160 hrs)
- └─ Design system extraction (80 hrs)
- └─ Typography setup (24 hrs)
- └─ Core navigation blocks (80 hrs)

Phase 2: Content Modeling (Weeks 7-8) ————— 200 hours

- └─ component-model.json (60 hrs)
- └─ component-definitions.json (60 hrs)
- └─ Content fragment models (40 hrs)
- └─ Import transformations (40 hrs)

Phase 3: Block Development (Weeks 9-14) ————— 1,080 hours

- └─ Hero blocks - 6 variants (120 hrs)
- └─ Card blocks - 10 variants (200 hrs)
- └─ Interactive blocks - 10 (280 hrs)
- └─ Form blocks - 4 (120 hrs)
- └─ Content blocks - 8 (160 hrs)
- └─ Product-specific blocks - 6 (200 hrs)

Phase 4: Page Review & Assets (Weeks 15-16) ——— 360 hours

- └─ Page review & re-authoring (200 hrs)
- └─ URL redirect mapping (40 hrs)
- └─ DAM asset migration (80 hrs)
- └─ Image optimization (40 hrs)

Phase 5: Edge Workers & APIs (Weeks 17-18) ——— 340 hours

- └─ Servlet/API migration (160 hrs)
- └─ Pricing API integration (60 hrs)
- └─ Lead form handling (40 hrs)
- └─ Search functionality (80 hrs)

Phase 6: AEM Migration (Weeks 19-20) ————— 280 hours

- └─ Custom functionality migration (120 hrs)
- └─ Meta-schema & taxonomy (80 hrs)
- └─ User/group migration (40 hrs)
- └─ Workflow configuration (40 hrs)

Phase 7: Integrations (Weeks 21-22) — 160 hours

— Analytics/tracking setup (60 hrs)

— Third-party scripts (40 hrs)

— Search indexing (40 hrs)

— Social meta tags (20 hrs)

Phase 8-9: Validation & Launch (Weeks 23-24) — 640 hours

— Functional validation (160 hrs)

— Accessibility audit (80 hrs)

— Performance testing (60 hrs)

— SEO validation (40 hrs)

— Security review (40 hrs)

— UAT & sign-off (80 hrs)

— DNS cutover (40 hrs)

— Author training (60 hrs)

— Hypercare & monitoring (80 hrs)

TOTAL PROJECT HOURS: 3,644 base + contingency = 4,800 hours

7. Resource Requirements

7.1 Team Structure

Role	Count	Responsibilities
Project Manager	1	Timeline, coordination, stakeholder management
Technical Lead	1	Architecture, code review, technical decisions
Senior EDS Developer	2	Core blocks, complex components, edge workers
Mid EDS Developer	2	Standard blocks, templates, CSS
Junior EDS Developer	1	Support, simple blocks, testing
Content Strategist	1	Content mapping, IA, CF models
Content Author	2	Content migration, DAM management
QA Engineer	1	Testing, validation, accessibility
SEO Specialist	0.5	SEO audit, redirect validation
DevOps/Admin	0.5	AEM admin, monitoring setup
Total	10-12	

7.2 Hours by Role per Phase

Role	Ph 0	Ph 1	Ph 2	Ph 3	Ph 4-6	Ph 7-9	Total
Project Manager	24	40	20	60	60	80	284
Technical Lead	64	80	100	120	120	80	564
Sr. EDS Dev 1	0	120	40	320	200	80	760
Sr. EDS Dev 2	0	100	40	280	200	80	700
Mid EDS Dev 1	0	80	0	200	160	80	520
Mid EDS Dev 2	0	40	0	160	120	60	380
Jr. EDS Dev	0	24	0	80	80	60	244
Content Strategist	40	20	80	40	80	40	300
Content Author 1	0	0	0	0	240	60	300
Content Author 2	0	0	0	0	160	40	200
QA Engineer	0	0	0	0	80	280	360
SEO Specialist	32	0	0	0	0	40	72
DevOps/Admin	0	0	0	0	60	60	120
Phase Totals	160	504	280	1,260	1,560	1,040	4,804

8. Cost Estimation

8.1 Labor Costs - By Role

Role	Rate/Hr	Hours	Total	Notes
Project Manager	\$150	284	\$42,600	Planning, coordination
Technical Lead	\$200	564	\$112,800	Architecture, decisions
Sr. EDS Developer 1	\$185	760	\$140,600	Core blocks, edge workers
Sr. EDS Developer 2	\$185	700	\$129,500	Complex components
Mid EDS Developer 1	\$165	520	\$85,800	Standard blocks
Mid EDS Developer 2	\$165	380	\$62,700	Templates, CSS
Jr. EDS Developer	\$140	244	\$34,160	Support, testing
Content Strategist	\$135	300	\$40,500	IA, content models
Content Author 1	\$95	300	\$28,500	Primary migration
Content Author 2	\$95	200	\$19,000	Secondary support
QA Engineer	\$130	360	\$46,800	Testing, ally
SEO Specialist	\$140	72	\$10,080	SEO validation
DevOps/Admin	\$160	120	\$19,200	Admin, monitoring
Subtotal Labor		4,804	\$772,240	

8.2 Labor Costs - By Phase

Phase	Hours	Labor Cost	% of Total
Phase 0: Pre-Migration	160	\$26,000	3%
Phase 1: Foundation	504	\$84,000	11%
Phase 2: Content Modeling	280	\$50,000	6%
Phase 3: Block Development	1,260	\$218,000	28%
Phase 4-6: Migration	1,560	\$248,000	32%
Phase 7-9: Validation/Launch	1,040	\$146,240	19%
Total	4,804	\$772,240	100%

8.3 Additional Costs

Item	Cost	Frequency	Annual Cost	Notes
Adobe EDS Licensing	TBD	Annual	TBD	Per Adobe agreement
AEM Cloud Service	TBD	Annual	TBD	Per Adobe agreement
Search Service (Algolia)	\$1,200/mo	Monthly	\$14,400	Enterprise search
Edge Worker Compute	\$500/mo	Monthly	\$6,000	Cloudflare/similar
Image CDN	\$300/mo	Monthly	\$3,600	Image optimization
Monitoring Tools	\$400/mo	Monthly	\$4,800	Datadog/New Relic
Subtotal Additional			\$28,800	First year

8.4 Contingency & Risk Buffer

Contingency Type	Base Amount	%	Buffer Amount
Scope contingency	\$772,240	10%	\$77,224
Technical risk buffer	\$218,000	15%	\$32,700
Integration risk	\$50,000	20%	\$10,000
Total Contingency			\$119,924

8.5 Total Cost Summary

Category	Amount
Labor (4,804 hours)	\$772,240
Additional Costs (Year 1)	\$28,800
Contingency (~15%)	\$119,924
Project Total	\$920,964

Cost Range Scenarios

Scenario	Hours	Cost	Notes
Optimistic	4,000	\$750,000	No major issues, experienced team
Expected	4,800	\$920,000	Planned estimate with contingency
Conservative	5,800	\$1,100,000	Complex issues, scope additions

9. Risk Assessment

9.1 Risk Matrix

Risk	Probability	Impact	Mitigation
Complex mega-menu navigation	High	High	Technical spike early, fallback options
Pricing API integration	Medium	High	Early API documentation, mock services
Content approval delays	High	High	Phased reviews, dedicated reviewers
AT&T brand compliance	Medium	High	Early brand team engagement
Edge worker complexity	Medium	High	Prototype critical workers first
Third-party script conflicts	Medium	Medium	Staged integration, testing
SEO ranking impact	Medium	High	Comprehensive redirect strategy
Performance with dynamic content	Medium	Medium	Caching strategy, edge optimization

9.2 Key Assumptions

- AT&T provides timely content approvals
- Access to existing AEM instance for content extraction
- API documentation available for backend services
- AT&T brand fonts licensed for EDS use
- ChiliPiper/OneTrust integrations continue as-is
- No major redesign required (visual refresh acceptable)

- Legal/compliance review integrated into timeline

10. Success Criteria

10.1 Technical Success Metrics

Metric	Target
Lighthouse Performance	> 90
Lighthouse Accessibility	> 95
Lighthouse SEO	> 95
Core Web Vitals (all)	Pass
Cross-browser compatibility	Chrome, Safari, Firefox, Edge
Mobile responsiveness	100% pages
Page load time (LCP)	< 2.5s

10.2 Business Success Metrics

Metric	Target
Page load time improvement	> 40%
Content authoring time	< 50% of current
Time to publish	< 5 minutes
Uptime SLA	99.9%
Lead form conversion	Maintain or improve
SEO rankings	No degradation

11. Appendices

Appendix A: Key URLs Inventory

Section	URL Pattern	Est. Pages
Products	/products/*.html	50+
Portfolios	/portfolios/*.html	7
Industries	/industries/*.html	12
Categories	/categories/*.html	20+
Learn/Insights	/learn/*.html	40+
Support	/support/*.html	5
Offers	/offers*.html	5+
Other	Various	60+
Total		200+

Appendix B: Integration Contacts

System	Owner	Contact
Adobe Analytics	AT&T Digital	TBD
ChiliPiper	Marketing Ops	TBD
OneTrust	Legal/Privacy	TBD
CRM/Lead System	Sales Ops	TBD
Business Center	IT	TBD

Appendix C: Content Fragment Models

To be developed during Phase 2.

12. Estimation Approaches: Manual vs EC/AEMCoder

This section compares traditional manual migration with the accelerated EC/AEMCoder approach. EC/AEMCoder uses AI-assisted tooling to automate initial block generation, content mapping, and markdown structure creation.

12.1 What EC/AEMCoder Automates

Capability	Automated	Manual Effort Remaining
Block structure generation	☐ Yes	Review and refinement
Initial HTML → Markdown conversion	☐ Yes	Content validation
Block CSS scaffolding	☐ Yes	Brand refinement, responsive tuning
Content mapping to blocks	☐ Yes	Edge case handling
Basic JavaScript decoration	☐ Partial	Complex interactions, state management
Image extraction & references	☐ Yes	DAM migration, optimization

12.2 What Still Requires Manual Work

Task	Why Manual	Effort Level
CSS brand refinement	AT&T brand compliance, pixel-perfect styling	High
Complex JavaScript interactions	Pricing calculators, dynamic filtering, animations	High
Accessibility compliance	WCAG 2.1 AA testing, ARIA attributes, keyboard nav	Medium
component-model.json	JCR package structure for AEM importer	Medium
component-definitions.json	Universal Editor field definitions	Medium
Edge workers	API proxies, form handling, personalization	High
Integration testing	Third-party scripts, analytics, CRM	Medium
Content validation	Business accuracy, legal review	High
Performance optimization	Core Web Vitals tuning, lazy loading	Medium

12.3 Hours Comparison by Phase

Phase	Manual Hours	EC/AEMCoder Hours	Savings	Notes
Phase 0: Pre-Migration	160	160	0	Same (planning, audits)
Phase 1: Foundation	424	284	140	Initial migration + block updates accelerated
Phase 2: Content Modeling	200	180	20	Slight assist on transformations
Phase 3: Block Development	1,080	600	480	Major acceleration (~45%)
Phase 4: Assets	360	360	0	Same (content review, DAM)
Phase 5: Edge Workers	340	340	0	Same (custom code required)
Phase 6: AEM Migration	280	280	0	Same (AEM configuration)
Phase 7: Integrations	160	160	0	Same (third-party scripts)
Phase 8-9: Validation/Launch	640	600	40	Fewer defects to fix
Contingency	1,156	1,156	0	Same % contingency
TOTAL	4,800	4,120	680	~14% reduction

12.4 Block Development Comparison (Phase 3)

Block Category	Manual (hrs)	EC/AEMCoder (hrs)	Reduction
Hero Blocks (6)	120	72	40%
Card Blocks (10)	200	100	50%
Interactive Blocks (10)	280	168	40%
Form Blocks (4)	120	72	40%
Content Blocks (8)	160	80	50%
Product-specific (6)	200	108	46%
TOTAL	1,080	600	~44%

12.5 Cost Comparison

Category	Manual	EC/AEMCoder	Savings
Labor (base hours)	\$772,240	\$659,200	\$113,040
Additional Costs (Year 1)	\$28,800	\$28,800	\$0
Contingency (~15%)	\$119,924	\$102,960	\$16,964
PROJECT TOTAL	\$920,964	\$791,000	~\$130,000

12.6 Timeline Comparison



13. Key Insights

13.1 EC/AEMCoder Value Proposition

Insight	Impact
Greatest impact on repetitive tasks	Card blocks, content blocks see 50% reduction
Complex components still need expertise	Pricing calculators, mega-menus require senior developers
Quality of output varies	Simple blocks: production-ready; Complex: 60-70% complete
Consistency across blocks	EC/AEMCoder maintains consistent patterns and CSS structure
Faster iteration cycles	Initial version in hours vs days enables more refinement time

13.2 When to Choose Each Approach

Choose Manual When	Choose EC/AEMCoder When
Small scope (< 20 pages)	Large scope (50+ pages)
Highly custom design	Standard EDS patterns
Complex interactive requirements	Content-heavy sites
Existing experienced EDS team	Team ramping up on EDS
Tight brand guidelines	Flexible brand implementation

13.3 Hybrid Recommendation for AT&T Business

Given the AT&T Business site characteristics:

- **200+ pages** → EC/AEMCoder advantageous for scale
- **Complex interactive components** → Manual expertise required
- **Strong brand guidelines** → CSS refinement essential
- **Enterprise integrations** → Edge workers manual regardless

Recommendation: EC/AEMCoder approach with senior developer oversight for complex blocks

RECOMMENDED BLOCK APPROACH BY COMPLEXITY

EC/AEMCoder Primary (50% effort reduction)

- cards-product, cards-feature, cards-industry
- columns, quote, table, embed, download
- hero-minimal, hero-split
- cta-banner, divider, icon-list
- breadcrumb, cards-link, cards-cta

EC/AEMCoder + Manual Refinement (30-40% reduction)

- hero-video, hero-carousel, hero-tabs
- cards-pricing, cards-testimonial, cards-stat
- accordion, tabs, modal
- lead-form, contact-form, newsletter
- offer-card, guarantee-banner

Manual Development Primary (10-20% reduction)

- header (mega-menu complexity)
- footer (multi-column, legal links)
- mobile-nav (nested interactions)
- pricing-calculator (dynamic logic)
- comparison-table (interactive features)
- search, filter (complex UX)
- video-modal (lightbox interactions)

14. Disclaimers & Assumptions

14.1 Estimate Disclaimers

⚠ IMPORTANT DISCLAIMERS

1. **Estimates are projections, not commitments.** Actual effort may vary $\pm 20\%$ based on discovered complexity, scope changes, and team velocity.

2. **EC/AEMCoder savings are based on typical outcomes.** Results depend on source site structure, content quality, and block complexity. Highly custom designs may see lower automation benefits.
3. **Timeline assumes no major scope changes.** Additions to scope, design revisions, or new integration requirements will extend timelines proportionally.
4. **Cost rates are illustrative.** Actual rates depend on staffing model (internal, SI partner, offshore blend) and regional variations.
5. **Contingency should not be eliminated.** The 15% contingency accounts for unknowns discovered during migration. Removing it increases project risk.

14.2 Technical Assumptions

Assumption	Risk if Invalid	Mitigation
Source AEM content is accessible	High - delays extraction	Early access validation
APIs have documentation	Medium - extends edge worker dev	Technical spike Week 3
Brand fonts are web-licensed	Low - fallback to system fonts	Legal review Week 2
No major redesign required	High - extends all phases	Stakeholder alignment
Third-party scripts compatible	Medium - integration issues	Staged testing

14.3 EC/AEMCoder-Specific Assumptions

Assumption	Impact if Wrong
Source HTML is semantic and well-structured	Lower automation quality, more manual fixes
Consistent page templates across site	Higher variance in block output
Standard CSS naming conventions	Additional CSS mapping required
Images accessible via public URLs	Manual asset handling needed
Content in English (primary)	Multi-language adds complexity

14.4 Organizational Assumptions

Assumption	Risk if Invalid
Content approvers available within 5 business days	Schedule delays
Single decision-maker for design/UX	Revision cycles
Legal review integrated into timeline	Launch delays
Training resources allocated	Adoption issues post-launch
Hypercare team identified	Post-launch support gaps

Document History

Version	Date	Author	Changes
1.0	Feb 2026	Migration Team	Initial document
1.1	Feb 2026	Migration Team	Added EC/AEMCoder comparison, Key Insights, Disclaimers

This migration plan is a living document and will be updated as the project progresses.
