

AT&T Business & FirstNet - Combined EDS Migration Plan

Executive Summary

This document outlines the comprehensive migration plan for migrating both **AT&T Business** (business.att.com) and **FirstNet** (firstnet.com) websites to AEM Edge Delivery Services (EDS) with Universal Editor (UE).

Combined Metrics

Metric	AT&T Business	FirstNet	Combined	With Synergies
Total Pages	~749	~700	~1,449	~1,449
Page Templates	12	10	22	14 (shared)
Unique Blocks	68 (consolidated)	58 (consolidated)	126	96 (after reuse)
Block Variations	117 original	106 original	223 original	consolidated
Shared Blocks	-	-	-	30 (built once)
Base Effort (hrs)	2,616-3,240	3,264-3,984	5,880-7,224	4,960-6,080
Duration	14-18 weeks	22-26 weeks	36-44 weeks	30-36 weeks
Team Size	5-7	6-8	11-15	8-10
Cost Estimate	\$687K-\$1.06M	\$1.07M-\$1.45M	\$1.76M-\$2.51M	\$1.42M-\$1.95M

Synergy Savings

- Effort Savings:** ~920-1,144 hours (16% reduction)
- Duration Savings:** 6-8 weeks (parallel execution)
- Cost Savings:** ~\$340K-\$560K

Site Overview

AT&T Business (business.att.com)

Category	Page Count
Homepage	1
Portfolio Pages	9
Product Pages	~150
Category Pages	~75
Industry Pages	~14
Business Solutions	~10
Learn - Content/Articles	~300
Learn - Customer Stories	~112
Support Pages	~60
Offers/Deals	~37
Regional/Areas	~15
Core Navigation	~15
TOTAL	~749

FirstNet (firstnet.com)

Category	Page Count
Homepage & Main Pages	5
Power of FirstNet	10
Coverage	11
Rate Plans	4
Devices - Phones	~175
Devices - Tablets/Other	~105
Industry Solutions	~70
Apps	~56
Community - News/Blogs	~140
Mission Critical	15
Support/Help	~105
Core Pages	~49
TOTAL	~700

Combined Page Inventory

Priority Distribution

Priority	AT&T Business	FirstNet	Combined
P0 (Must Have)	~100	~150	~250
P1 (Should Have)	~350	~300	~650
P2 (Nice to Have)	~299	~250	~549
TOTAL	~749	~700	~1,449

Page Type Comparison

Page Type	AT&T Business	FirstNet	Notes
Homepage	1	5	Different layouts
Product/Device Pages	~150	~280	FirstNet device-heavy
Industry/Solution Pages	~24	~70	Similar structure
Article/Content Pages	~412	~140	AT&T content-heavy
Support Pages	~60	~105	FirstNet more comprehensive
Offer Pages	~37	~30	Similar structure
Core/Landing Pages	~65	~70	Similar structure

Shared Components & Synergies

Block Reusability Analysis

Consolidated Block Counts:

- AT&T Business: **68 consolidated blocks** (from 117 original variations)
- FirstNet: **58 consolidated blocks** (from 106 original variations)
- **Combined Total:** 126 blocks
- **Truly Shared (built once):** 30 blocks
- **Effective Unique Blocks:** 96 blocks (66 AT&T-only/unique + 30 shared)

Block Category	AT&T Business	FirstNet	Shared Blocks	Reuse %	Hours Saved
Header/Navigation	2 blocks	3 blocks	2 (Quick Links, Anchor Nav)	80%	32 hrs
Footer	1 block	1 block	1 (Footer)	85%	24 hrs
Hero Blocks	7 variants	6 variants	1 (Base Hero Component)	65%	48 hrs
Card Carousels	4 blocks	4 blocks	3 (Offer, Product, Story Cards)	75%	72 hrs
Feature/Value Props	2 blocks	3 blocks	2 (Feature Grid, Value Props)	70%	40 hrs
Form Blocks	4 blocks	3 blocks	2 (Email Sub, Form Base)	55%	36 hrs
FAQ/Accordion	3 blocks	2 blocks	1 (Accordion Base)	90%	32 hrs
CTA/Promo Banners	5 blocks	4 blocks	3 (Promo, Contact CTA, Banner)	80%	56 hrs
Table/Comparison	3 blocks	3 blocks	2 (Comparison, Data Table)	70%	40 hrs
Article/Content	8 blocks	3 blocks	2 (Article Card, Content Block)	55%	36 hrs
Support Blocks	6 blocks	4 blocks	2 (Support Grid, Contact Cards)	65%	40 hrs
Video Blocks	2 blocks	1 block	1 (Video Embed)	85%	24 hrs
Industry/Solution	3 blocks	4 blocks	2 (Solution Cards, Image+Text)	55%	32 hrs
Customer Story	3 blocks	2 blocks	2 (Stats Block, Story Card)	75%	28 hrs
Offer-Specific	4 blocks	3 blocks	2 (Offer Cards, Pricing Pattern)	65%	32 hrs
Link/Navigation	4 blocks	2 blocks	1 (Link List)	60%	16 hrs
Miscellaneous	7 blocks	10 blocks	1 (Error Page)	40%	12 hrs
TOTALS	68 blocks	58 blocks	30 shared	~67% avg	~600 hrs

Site-Specific Blocks (No Reuse):

- **AT&T Business Only (~38 blocks):** RAI Lead Form, Check Availability, Article Tags/Share/Quote, Guided Courses, Business Center CTA, International Calling, Award Badges, etc.
- **FirstNet Only (~28 blocks):** Interactive Map, Device Gallery/Detail, Eligibility Forms, App Carousel/Features, Why FirstNet Section, FirstNet Promise, History Text, etc.

Template Reusability

Template	AT&T Business	FirstNet	Shared	Hours Saved
homepage	Yes	Yes	No (different layouts)	0 hrs
product/device	Yes	Yes	Partial (60% shared)	24 hrs
category/industry	Yes	Yes	Yes (80% shared)	32 hrs
article	Yes	Yes	Yes (90% shared)	28 hrs
support	Yes	Yes	Yes (85% shared)	24 hrs
offers	Yes	Yes	Yes (75% shared)	20 hrs
landing	Yes	Yes	Yes (70% shared)	16 hrs
regional/campaign	Yes	Yes	Partial (50% shared)	12 hrs

Template Savings: ~156 hours

Integration Reusability

Integration	AT&T Business	FirstNet	Shared	Hours Saved
Adobe Analytics	Yes	Yes	Yes (90% shared)	40 hrs
Adobe Target	Yes	Yes	Yes (90% shared)	40 hrs
Marketo/Eloqua	Yes	Yes	Yes (80% shared)	32 hrs
Chat Widget	Yes	Yes	Yes (100% shared)	24 hrs
Fastly CDN	Yes	Yes	Yes (100% shared)	28 hrs
CI/CD Pipeline	Yes	Yes	Yes (100% shared)	20 hrs

Integration Savings: ~184 hours

Combined Phase Breakdown

Phase 1: Foundation & Shared Infrastructure

Duration: 3-4 weeks | **Effort:** 320-400 hours

Task	Hours	Notes
Shared EDS project setup	32	Monorepo or multi-site
GitHub/SharePoint integration	24	Shared infrastructure
AEM Universal Editor setup	48	Single UE instance
Shared design tokens	48	Brand-specific overrides
Global styles framework	40	Theming support
Shared header component	40	Brand variants
Shared footer component	32	Brand variants
Navigation structure (both)	32	Separate navs
CI/CD pipeline	24	Shared deployment
Phase 1 Total	320	

Phase 2: Core Blocks Development (Shared)

Duration: 6-7 weeks | **Effort:** 800-950 hours

Task	Hours	Notes
Hero block (all variants)	96	9 total variants
Cards block (all variants)	160	16 total variants
Carousel block	80	6 variants
Tabs block	48	5 variants
Accordion block	36	4 variants
Form block	100	7 variants
CTA-banner block	48	6 variants
Table block	60	7 variants
Video block	36	4 variants
Breadcrumb block	16	Shared
Columns block	20	Shared
Fragment support	24	Shared
UE component models	80	Both sites
Block documentation	40	Combined docs
QA & testing	64	Both sites
Phase 2 Total	908	

Phase 3: Site-Specific Blocks

Duration: 3-4 weeks | Effort: 360-440 hours

AT&T Business Specific

Task	Hours
Promo-banner block	48
Link-list block	32
Search-results block	52
RAI form integration	40
AT&T-specific UE config	32
AT&T Subtotal	204

FirstNet Specific

Task	Hours
Icon-nav block	36
Device-gallery block	60
Value-props block	40
Eligibility form	48
FirstNet-specific UE config	32
FirstNet Subtotal	216

Phase 3 Total: 420 hours

Phase 4: Template Development

Duration: 4-5 weeks | Effort: 520-640 hours

Shared Templates

Template	Hours	Sites
Article template	32	Both
Support template	28	Both
Category/Industry template	36	Both
Offers template	32	Both
Landing template	32	Both
Shared Subtotal	160	

AT&T Business Templates

Template	Hours
Homepage	40
Portfolio	28
Product	36
Regional	20
Partner	20
AT&T Subtotal	144

FirstNet Templates

Template	Hours
Homepage	40
Device	56
Plans	32
Feature/Mission Critical	32
Coverage	28
Sign-up	32
FirstNet Subtotal	220

Phase 4 Total: 524 hours

Phase 5: Integrations

Duration: 4-5 weeks | Effort: 440-540 hours

Shared Integrations

Integration	Hours	Notes
Adobe Analytics	48	Both sites
Adobe Target	48	Both sites
Marketo/Eloqua forms	48	Both sites
Chat widget	28	Both sites
Fastly CDN	32	Both sites
Performance optimization	40	Both sites
Shared Subtotal	244	

AT&T Business Specific

Integration	Hours
ChiliPiper calendar	28
Search (Coveo/Algolia)	44
AT&T Subtotal	72

FirstNet Specific

Integration	Hours
Eligibility API	48
LocalControl/SSO	56
FirstNet Subtotal	104

Phase 5 Total: 420 hours

Phase 6: Content Migration

Duration: 8-10 weeks | Effort: 1,100-1,400 hours

Import Script Development

Task	Hours
Shared import framework	80
AT&T Business parsers	60
FirstNet device parsers	80
Script Subtotal	220

AT&T Business Migration

Wave	Pages	Hours
Wave 1 (P0)	~100	84
Wave 2 (P1)	~300	177
Wave 3 (P2)	~300	64
Asset migration	-	32
Redirects (700+)	-	32
QA validation	-	48
AT&T Subtotal	~700	437

FirstNet Migration

Wave	Pages	Hours
Wave 1 (P0)	~220	159
Wave 2 (P1)	~450	161
Wave 3 (P2)	~520	138
Asset migration	-	48
Redirects (1,200+)	-	48
QA validation	-	72
FirstNet Subtotal	~1,187	626

Phase 6 Total: 1,283 hours

Phase 7: Testing & Launch

Duration: 4-5 weeks | Effort: 480-580 hours

Task	Hours	Notes
Cross-browser testing	56	Both sites
Mobile/responsive testing	64	Both sites
Accessibility (WCAG 2.1)	72	Both sites
Performance (Lighthouse)	48	Both sites
SEO validation	40	Both sites
Security testing	40	Both sites
UAT support	56	Both sites
Bug fixes & refinements	80	Both sites
DNS cutover planning	16	Both sites
Go-live execution	16	Staged rollout
Post-launch monitoring	32	Both sites
Phase 7 Total	520	

Total Effort Summary

Without Synergies (Sequential)

Phase	AT&T Business	FirstNet	Total
Foundation	248	264	512
Core Blocks	704	740	1,444
Templates	416	464	880
Secondary Blocks	304	272	576
Integrations	284	368	652
Content Migration	515	745	1,260
Testing & Launch	284	352	636
TOTAL	2,755	3,205	5,960

With Synergies (Combined)

Phase	Hours	Savings	Savings Source
Foundation & Shared Infrastructure	320	192	Shared repo, CI/CD, design tokens
Core Blocks (30 Shared)	600	844	Build shared blocks once (~600 hrs saved)
Site-Specific Blocks (66 unique)	760	-184	ATT: 38 blocks, FN: 28 blocks
Template Development	524	356	8 shared templates (~156 hrs)
Integrations	468	184	Analytics, CDN, chat shared
Content Migration	1,200	60	Shared import framework
Testing & Launch	520	116	Shared test infrastructure
TOTAL	4,392	1,568	

With 20% contingency: 5,270 hours


Synergy Breakdown

Category	Hours Saved	Details
Shared Blocks (30 blocks)	~600 hrs	Hero, Carousels, Forms, FAQ, CTAs, Tables, etc.
Shared Templates (8 templates)	~156 hrs	Article, Support, Category, Offers, Landing, etc.
Shared Integrations	~184 hrs	Analytics, Target, CDN, CI/CD
Shared Infrastructure	~192 hrs	Design tokens, repo setup, staging
Total Synergy Savings	~1,132 hrs	

Savings Summary

Metric	Sequential	Combined	Savings
Total Hours	5,960	4,392	1,568 hrs (26%)
With Contingency	7,152	5,270	1,882 hrs
Duration	36-44 weeks	30-36 weeks	6-8 weeks
Team Size	11-15 FTEs	8-10 FTEs	3-5 FTEs

Combined Timeline

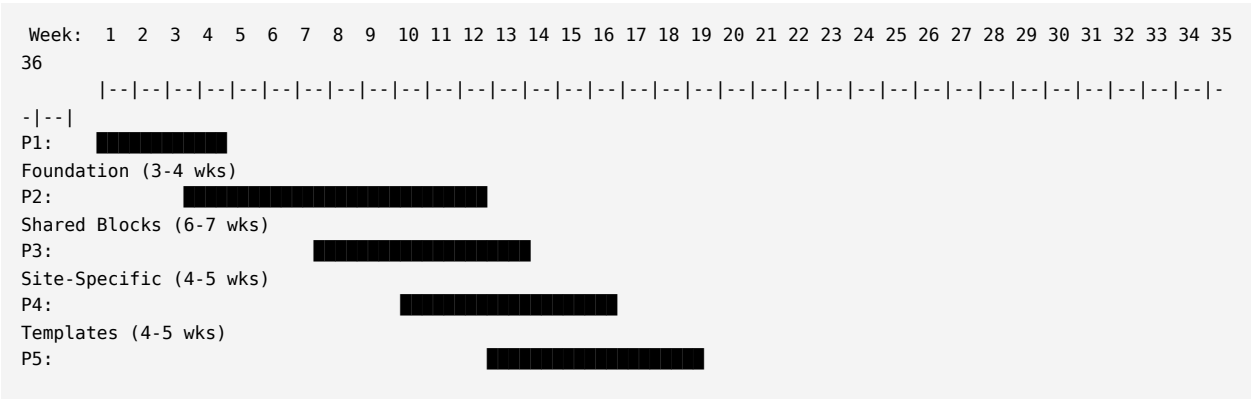

Integrations (4-5 wks)	
P6-ATT:	
AT&T Migration (8 wks)	
P6-FN:	
FirstNet Migration (10 wks)	
P7:	
Testing/Launch (4-5 wks)	
____Shared Foundation____ __Shared Blocks__ ____Parallel Migration____ __QA & Launch____	

Milestone Schedule

Milestone	Week	Description
Project Kickoff	1	Team onboarding, environment setup
Foundation Complete	4	Shared infrastructure ready
Shared Blocks Complete	11	30 shared blocks functional
Site-Specific Blocks	16	All 96 blocks ready for both sites
Templates Complete	21	All 14 page templates ready
Integrations Complete	25	All third-party integrations
AT&T Business P0 Launch	28	AT&T Business core pages live
FirstNet P0 Launch	30	FirstNet core pages live
Full Migration Complete	34	All 1,449 pages migrated
Final Launch	36	Both sites fully launched

Resource Requirements

Combined Team Composition

Role	Count	Phases	Allocation
Program Manager	1	All	100%
Tech Lead / Architect	1	All	100%
EDS/Frontend Developer	4	1-5, 7	100%
UE Configuration Specialist	1	2-4	100%
Content Migration Lead	1	6	100%
Content Migration Specialist	2	6	100%
QA Lead	1	All	100%
QA Engineer	1	All	75%
DevOps Engineer	1	1, 5, 7	50%
TOTAL	14		

Effective FTEs: 8-10

Skill Matrix

Skill	Required For	Team Members
EDS/Franklin Development	Blocks, Templates	4 Developers
Universal Editor	UE Configuration	1 Specialist + Developers
Adobe Analytics/Target	Integrations	1 Developer
AT&T APIs (SSO, LocalControl)	FirstNet Integrations	1 Developer
Content Migration	Import Scripts	1 Lead + 2 Specialists
QA/Testing	All Phases	1 Lead + 1 Engineer

Cost Estimation

Combined Cost Breakdown (With Synergies)

Resource Type	Hours	Rate Range	Cost Range
Program Manager	350	\$150-175/hr	\$52,500-61,250
Tech Lead	550	\$150-200/hr	\$82,500-110,000
Senior Developer (×3)	1,800	\$125-175/hr	\$225,000-315,000
UE Specialist	350	\$125-150/hr	\$43,750-52,500
Content Lead	280	\$100-125/hr	\$28,000-35,000
Content Specialist (×2)	500	\$75-100/hr	\$37,500-50,000
QA Lead	350	\$125-150/hr	\$43,750-52,500
QA Engineer	280	\$100-125/hr	\$28,000-35,000
DevOps	160	\$125-150/hr	\$20,000-24,000
BASE TOTAL	4,620		\$561,000-735,250
Contingency (20%)	924	-	\$112,200-147,050
GRAND TOTAL	5,544		\$673,200-882,300

Cost Comparison

Approach	Hours	Cost Range	Notes
Sequential (separate projects)	7,152	\$930K-\$1.18M	Full teams for each site
Combined (with synergies)	5,270	\$673K-\$882K	Shared resources
Savings	1,882 hrs	\$257K-\$298K	~26% reduction

Cost Per Page

Metric	Sequential	Combined
Total Pages	1,449	1,449
Cost per Page	\$642-\$814	\$465-\$609
Savings per Page	-	\$177-\$205

Risk Assessment

Risk	Probability	Impact	Mitigation
Resource contention between sites	High	Medium	Clear sprint allocation, dedicated leads
Scope creep from stakeholders	Medium	High	Fixed scope phases, change control
Integration complexity	Medium	High	Early POCs, parallel development
Brand consistency challenges	Medium	Medium	Shared design system with overrides
Timeline slippage	Medium	High	Buffer in schedule, phased delivery
Content volume underestimated	Medium	Medium	Automated import, bulk tools
UE configuration complexity	Medium	Medium	Dedicated UE specialist
Third-party API delays	Medium	High	Fallback options, early testing

Success Criteria

Metric	Target	AT&T Business	FirstNet
Lighthouse Performance	> 90	Yes	Yes
Lighthouse Accessibility	> 95	Yes	Yes
Page Load Time (LCP)	< 2.5s	Yes	Yes
Content Migration Accuracy	> 99%	Yes	Yes
Zero Critical Bugs at Launch	Yes	Yes	Yes
Author Training Completion	100%	Yes	Yes
Redirect Coverage	> 99.5%	Yes	Yes

Governance & Communication

Steering Committee

- Monthly executive reviews
- Go/No-go decisions for launches
- Budget and scope approvals

Project Cadence

- Daily standups (15 min)
- Weekly sprint reviews
- Bi-weekly stakeholder demos
- Monthly steering committee

Decision Making

Decision Type	Authority
Technical architecture	Tech Lead
Sprint priorities	Program Manager
Scope changes	Steering Committee
Launch approval	Steering Committee

Appendix A: Combined Block Inventory

AT&T Business Blocks (68 Consolidated)

Category	Block Type	Variations	Complexity
Global	Quick Links Carousel	1	Medium
	Anchor Navigation	Multiple Pages	Medium
Hero	Hero Block	7 (Homepage Offer Cards, Homepage Video, Product, Portfolio/Industry, Content, Regional, 404)	High
Pricing	Pricing Cards Carousel	Product Pages	High
Features	Feature Cards Grid	Multiple Pages	Medium
	Value Props Grid	Portfolio/Landing	Medium
Carousels	Product/Service Cards Carousel	Multiple Pages	High
	Offer Cards Carousel	Multiple Pages	High
	Resource/Insights Cards	Multiple Pages	Medium
	Story Cards Overlay	Multiple Pages	Medium
Forms	Lead Form (RAI)	Multiple Pages	High
	Check Availability Form	Portfolio	Medium
	Email Subscription Form	Multiple Pages	Medium
	Search Block	404/Support	Medium
FAQ	FAQ Accordion	Multiple Pages	Medium
	Support Tabs Accordion	Support	Medium
	Features Collapsible List	Products	Medium
CTA	Promo Banner	Multiple Pages	Low
	Full-width Promo Banner	Multiple Pages	Medium
	Contact CTA Banner	Multiple Pages	Medium
	Multi-Button CTA	Portfolios	Low
	Current Customer CTA	Landing Pages	Low
Trust	Guarantee Checklist	Multiple Pages	Low
	Award Badge	Multiple Pages	Low
	Customer Testimonials Carousel	Why AT&T	Medium
Tables	Comparison Table	Multiple Pages	High
	Benefits Table	Category Pages	Medium
	Use Cases Table	Business Solutions	Medium
Content	Featured Article Block	Learn Hub	Medium
	Latest Articles Grid	Learn Hub	Medium

Category	Block Type	Variations	Complexity
	Article Header with Byline	Learn Articles	Low
	Article Tags	Learn Articles	Low
	Shareable Quote Block	Learn Articles	Low
	Social Share Block	Learn Articles	Low
	More Stories Grid	Learn Articles	Medium
	Top Topics Carousel	Learn Hub	Medium
Support	Support Quick Actions Grid	Support Pages	Medium
	Support Portal Cards	Support	Medium
	Resource Cards (Blue)	Support	Medium
	Guided Courses Block	Support	Medium
	Contact Tables	Contact	Medium
	Support Contact Block	Products	Low
Industry	Solution Link Cards	Industry Pages	Medium
	Image + Text Split	Multiple Pages	Medium
	Partner Cards Grid	Partner Solutions	Medium
Stories	Highlights/Stats Block	Customer Stories	Medium
	About Section	Customer Stories	Medium
	Case Study Stats Block	Portfolios	Medium
Video	Video Embed Block	Portfolios	Medium
	Video Content Cards	Portfolios	Medium
Links	Link List Block	Multiple Pages	Low
	Additional Resources Grid	Why AT&T	Low
	Helpful Links Cards	404	Low
	Solutions Sidebar	Learn Articles	Low
Offers	Featured Offers Cards	Offers	Medium
	Category Offers Carousel	Offers	Medium
	Referral Program Block	Offers	Low
	Risk-Free Trial Block	Multiple Pages	Low
Misc	Complete Solution Promo	Bundles	Medium
	Related Products Cards	Business Solutions	Medium
	International Calling Block	Phone Product	Low
	Contact Options 2-Column	Why AT&T	Low

Category	Block Type	Variations	Complexity
	Business Center CTA Card	Business Solutions	Low
	Data-driven Insights Cards	5G Portfolio	Medium

FirstNet Blocks (58 Consolidated)

Category	Block Type	Variations	Complexity
Global	Header Navigation	Global	High
	Footer	Global	Medium
	Email Subscription Form	Global	Medium
Hero	Hero Block	6 (Homepage, Standard, Product, Industry, Conversion, Device Detail)	High
Navigation	Quick Links Carousel	Multiple Pages	Medium
	Anchor Navigation	Multiple Pages	Medium
Products	Product Cards Grid	Device Categories	High
	Product Cards by Brand	Brand Grouping	Medium
	Industry Category Cards	Industry	Medium
Offers	Offer Cards Carousel	Multiple Pages	High
	Pricing Cards	Plans	High
	Plan Comparison	Offers	Medium
Features	Value Props Section	Multiple Pages	Medium
	Benefits Grid/Row	Multiple Pages	Medium
	Connectivity Ecosystem	Coverage	Medium
FAQ	FAQ Accordion	Multiple Pages	Medium
	Help Accordion	Help Pages	Medium
Stories	Customer Stories Carousel	Multiple Pages	High
	Case Study Feature	Multiple Pages	Medium
CTA	Contact CTA Banner	Multiple Pages	Medium
	Promo Banner	Multiple Pages	Low
	Download CTA Banner	Apps	Low
Conversion	Get Started Cards	Multiple Pages	Medium
	Eligibility Cards	Conversion	Medium
Content	News/Article Cards	Multiple Pages	Medium
	Article Content Block	News Articles	Medium
	Blogs/Videos Tabs	Community	Medium
Support	Popular Topics Grid	Help	Medium
	Help Links Cards	FAQ	Low
	Contact Cards Grid	Contact	Medium
	Need Help Section	Eligibility	Low
Apps	App Carousel	Apps	High

Category	Block Type	Variations	Complexity
	App Feature Section	Apps	Medium
	Developer Program Section	Apps	Low
Industry	Why FirstNet Section	Industry Detail	Medium
	Appreciation Section	Industry Detail	Medium
	Customer Quote Block	Industry Detail	Low
	Features Carousel	Industry Detail	Medium
Tables	Comparison Image	Why FirstNet	Low
	Impacts Table	Eligibility	High
	Document Cards	Eligibility	Medium
Specialty	Interactive Map	Coverage	High
	Video Feature Block	Power	Medium
	History Text Section	Power	Low
	Audience Cards	Why FirstNet	Medium
	FirstNet Promise	Why FirstNet	Medium
	Solutions Product Cards	Mission Critical	Medium
Legal	Legal Disclaimers	Multiple Pages	Low
	PDF Download Links	Plans	Low
	Shop Now CTA	Device Detail	Low
	Compatibility Link	Devices	Low
	Warning Note	Eligibility	Low
Error	Error Page Content	404	Low
	Recommended Pages List	404	Low

Combined Totals

Metric	AT&T Business	FirstNet	Combined
Consolidated Blocks	68	58	126
Original Variations	117	106	223
Shared/Reusable	~45	~35	~75 (with synergies)
Site-Specific	~23	~23	~46

Appendix B: Combined Page Inventory Summary

AT&T Business Pages (~749)

Category	% of Total	Est. Count
Content/Articles	40%	~300
Product Pages	20%	~150
Customer Stories	15%	~112
Industry/Category	10%	~75
Support/Help	8%	~60
Landing/Promo	5%	~37
Core Navigation	2%	~15
TOTAL	100%	~749

FirstNet Pages (~700)

Category	% of Total	Est. Count
Devices (Phones)	25%	~175
Devices (Tablets/Other)	15%	~105
Community/News	20%	~140
Help/Support	15%	~105
Industry Solutions	10%	~70
Apps	8%	~56
Core Pages	7%	~49
TOTAL	100%	~700

Combined Totals

Priority	AT&T Business	FirstNet	Combined
P0 (Must Have)	~100	~150	~250
P1 (Should Have)	~350	~300	~650
P2 (Nice to Have)	~299	~250	~549
TOTAL	~749	~700	~1,449

Appendix C: Detailed URL Lists

AT&T Business - Key Pages

See [ATT-BUSINESS-PAGE-INVENTORY.md](#) for complete URL listing including:

- 9 Portfolio pages

- 75+ Product pages
- 25+ Category pages
- 200+ Article pages
- 50+ Regional pages
- 60+ Partner pages

FirstNet - Key Pages

See [FIRSTNET-PAGE-INVENTORY.md](#) for complete URL listing including:

- 198 Phone pages
- 88 Tablet pages
- 21 Smart Device pages
- 39 Connected Device pages
- 90+ Industry Solution pages
- 180+ News articles

Appendix D: Integration Matrix

Integration	AT&T Business	FirstNet	Shared Code
Adobe Analytics	✓	✓	90%
Adobe Target	✓	✓	90%
Marketo Forms	✓	✓	80%
Eloqua Forms	✓	✓	80%
ChiliPiper	✓	-	0%
Coveo/Algolia Search	✓	-	0%
Chat Widget	✓	✓	100%
Feedback Widget	-	✓	0%
LocalControl	-	✓	0%
AT&T SSO	-	✓	0%
Eligibility API	-	✓	0%
Fastly CDN	✓	✓	100%

Next Steps

Immediate Actions (Week 1-2)

1. Stakeholder alignment meeting
2. Team assembly and onboarding
3. Environment setup
4. Design system review
5. Integration API access requests

Discovery Phase (Week 2-4)

1. Complete content audit
2. Integration POCs
3. UE configuration planning
4. Migration script prototypes
5. Risk mitigation planning

Sprint 0 (Week 4-5)

1. Technical spikes
2. Architecture finalization
3. Shared component library setup
4. CI/CD pipeline configuration
5. First block prototypes

Document Version: 2.1 Combined Total Pages: ~1,449 AT&T Business: 68 consolidated blocks (from 117 variations) FirstNet: 58 consolidated blocks (from 106 variations) Shared Blocks: 30 (built once for both sites) Effective Unique Blocks: 96 Combined Total Effort: 5,270 hours (with 20% contingency) Synergy Savings: ~1,568 hours (26%) Combined Duration: 30-36 weeks Cost Estimate: \$673K-\$882K (with synergies) Created: January 2026 Last Updated: January 2026
