

AT&T Business & FirstNet

Combined EDS Migration - Executive Summary

Project Overview

Migration of **AT&T Business** (business.att.com) and **FirstNet** (firstnet.com) to AEM Edge Delivery Services with Universal Editor, leveraging shared infrastructure for significant cost and time savings.


Key Metrics at a Glance

Metric	Value
Total Pages	1,449
Blocks to Build	96 (30 shared + 66 site-specific)
Duration	28-34 weeks
Team Size	8-10 FTEs
Total Investment	\$608K - \$797K


Combined Approach Savings

Category	Sequential Approach	Combined Approach	
Effort	6,785 hours	4,850 hours	1,935 hours (29%)
Duration	36-44 weeks	28-34 weeks	6-10 weeks
Cost	\$850K - \$1.05M	\$608K - \$797K	\$242K - \$253K
Cost/Page	\$587 - \$724	\$420 - \$550	\$167 - \$174

Synergy Sources

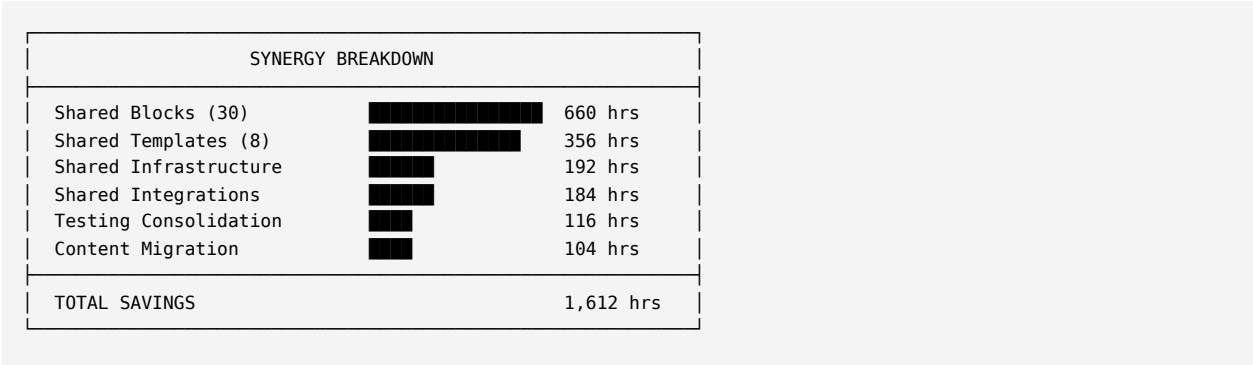

Project Timeline

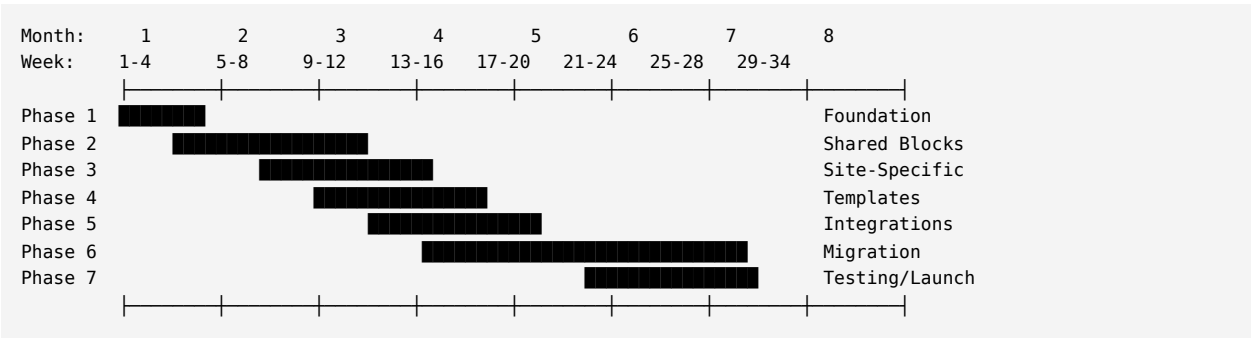

Key Milestones

Milestone	Week	Deliverable
Foundation Complete	4	Shared infrastructure, design tokens, CI/CD
Shared Blocks Complete	11	30 reusable blocks for both sites
All Blocks Ready	16	96 total blocks ready for authoring
Templates Complete	21	14 page templates configured
AT&T Business P0 Launch	28	Core AT&T Business pages live
FirstNet P0 Launch	30	Core FirstNet pages live
Full Migration Complete	34	All 1,449 pages migrated

Site Breakdown

AT&T Business (749 pages)

- Product & Portfolio pages
- Learn hub with 400+ articles
- Customer stories & case studies
- Support & offers pages

FirstNet (700 pages)

- 280+ device product pages
- Industry solutions (8 verticals)
- Community news & blogs
- Help center & eligibility flows

Investment Breakdown

Resource	Hours	Cost Range
Program Manager	320	\$48K - \$56K
Tech Lead	500	\$75K - \$100K
Senior Developers (3)	1,650	\$206K - \$289K
UE Specialist	320	\$40K - \$48K
Content Team (3)	660	\$56K - \$72K
QA Team (2)	560	\$64K - \$78K
DevOps	140	\$18K - \$21K
Contingency (20%)	830	\$101K - \$133K
TOTAL	4,980	\$608K - \$797K

Risk Mitigation

Risk	Impact	Mitigation
Resource contention	Medium	Dedicated leads per site, clear sprint allocation
Scope creep	High	Fixed scope phases, change control process
Integration delays	High	Early POCs, parallel development tracks
Timeline slippage	High	20% contingency buffer, phased delivery

Success Criteria

Metric	Target
Lighthouse Performance	> 90
Lighthouse Accessibility	> 95
Page Load Time (LCP)	< 2.5s
Content Migration Accuracy	> 99%
Redirect Coverage	> 99.5%

Recommendation

Proceed with the combined approach to realize:

- 29% cost savings (\$242K - \$253K)
- 6-10 weeks faster delivery
- Unified design system across both AT&T properties
- Reduced maintenance burden with shared components

Next Steps

1. **Stakeholder Alignment** - Confirm scope and timeline
 2. **Team Assembly** - Secure 8-10 FTE resources
 3. **Environment Setup** - AEM EDS project initialization
 4. **Design System Review** - Finalize brand tokens
 5. **Sprint 0 Kickoff** - Technical spikes and architecture
-

Document Version: 1.0 Based on: ATT-COMBINED-MIGRATION-PLAN.md v2.4 Date: January 2026
