

AbbVie.com Migration Plan

Adobe Edge Delivery Services (EDS) Migration

Source: <https://www.abbvie.com/> **Target Platform:** Adobe Edge Delivery Services (EDS) **Authoring:** Universal Editor with AEM as Content Source **Document Version:** 1.0 **Date:** February 2026

Executive Summary

This document outlines the comprehensive migration plan for AbbVie.com to Adobe Edge Delivery Services using **Universal Editor with AEM as the content source**. This architecture combines the performance benefits of EDS delivery with enterprise-grade content management in AEM, providing visual WYSIWYG authoring while maintaining existing content governance workflows.

The migration scope includes approximately **80-100 unique pages** across 5 main content sections, with complex interactive components including product catalogs (150+ products), drug pipeline data visualization, story/article content hub, and rich media integration.

Architecture Approach

Component	Technology	Purpose
Content Source	AEM Content Repository	Enterprise content storage, governance, workflows
Authoring	Universal Editor	Visual WYSIWYG editing experience
Delivery	Edge Delivery Services	High-performance CDN delivery, Core Web Vitals
Code Repository	GitHub	Block code, styles, scripts

Key Benefits of UE + AEM Architecture:

- Preserves existing AEM content governance and permissions
- Visual editing with real-time preview
- Sub-second page loads via EDS global CDN
- Lighthouse scores > 90 with minimal effort
- Seamless integration with existing AEM workflows

Key Metrics

Metric	Value
Total Estimated Pages	80-100
Product Entries	150+
Pipeline Compounds	90+
Content Stories	50+ (estimated)
Custom Blocks Required	35
Estimated Duration	18 weeks
Total Project Hours	2,920 hours
Team Size	7-9 FTEs
Estimated Cost	\$560,000 (with contingency)

1. Site Structure Analysis

1.1 Information Architecture

```
abbvie.com/
├── Homepage (1)
├── Who We Are/ (7 pages)
│   ├── Our Principles
│   ├── Operating with Integrity
│   ├── Key Facts
│   ├── Our Leaders
│   ├── Policies & Disclosures
│   ├── Our Stories (Content Hub - 50+ articles)
│   └── Pre-Approval Access Policy
├── Science/ (9 pages)
│   ├── Areas of Focus
│   ├── Areas of Innovation
│   ├── Pipeline (Complex data table)
│   ├── Our People
│   ├── Research Publications
│   ├── Partner with Us
│   ├── Clinical Trials
│   ├── R&D Sites
│   └── Independent Educational Grants
├── Patients/ (4 pages)
│   ├── Patient Support
│   ├── Patient Assistance
│   ├── Product Quality & Safety
│   └── Products (150+ product accordions)
├── Join Us/ (9 pages)
│   ├── Opportunities (6 sub-pages)
│   ├── Life at AbbVie
│   └── Benefits
├── Sustainability/ (10 pages)
│   ├── AbbVie Foundation (3 sub-pages)
│   ├── Disaster Relief
│   ├── ESG (3 sub-pages)
│   └── Philanthropy (2 sub-pages)
└── Utility Pages (8+)
    ├── Contact Center
    ├── Accessibility Statement
    ├── Site Map
    ├── Terms of Use
    ├── Privacy Notice
    └── Latest Earnings
```

1.2 Page Template Classification

Template Type	Count	Complexity	Examples
Homepage	1	High	Rich media, carousels, video
Section Landing	5	Medium-High	Who We Are, Science, Patients, Join Us, Sustainability
Content Hub	2	High	Our Stories, Pipeline
Article/Story	50+	Medium	Individual story pages
Product Listing	1	High	Products page with 150+ accordions
Standard Content	30+	Low-Medium	Policies, support pages
Leader Profile	10+	Medium	Executive bios
Data Table	1	High	Pipeline with filtering
Utility	8	Low	Contact, Terms, Privacy

2. Content Volume Estimation

2.1 Page Count by Section

Section	Static Pages	Dynamic/Generated	Total
Homepage	1	0	1
Who We Are	7	50+ stories	57+
Science	9	0	9
Patients	4	0	4
Join Us	9	0	9
Sustainability	10	0	10
Utility	8	0	8
Total	48	50+	98+

2.2 Content Elements Inventory

Element Type	Estimated Count
Hero sections	40+
Card components	200+
Video embeds	30+
Forms	5-10
Data tables	2-3
Accordions	150+ (products)
Carousels	15+
Images	500+
PDFs/Documents	50+

3. Block Requirements

3.1 Required EDS Blocks

Navigation Blocks (3)

Block Name	Complexity	Notes
header	High	Mega menu, search, language selector
footer	Medium	Multi-column, social links
breadcrumb	Low	Standard hierarchy

Hero Blocks (5)

Block Name	Complexity	Notes
hero-video	High	Background video with overlay text
hero-image	Medium	Standard hero with CTA
hero-carousel	High	Multiple slides
hero-split	Medium	Two-column layout
hero-minimal	Low	Text-only section header

Card Blocks (8)

Block Name	Complexity	Notes
cards	Medium	Standard grid cards
cards-story	Medium	Article preview with image, date, category
cards-stats	Medium	Large numbers with descriptions
cards-feature	Medium	Icon/image with text
cards-cta	Low	Simple call-to-action cards
cards-news	Medium	Press release listings
cards-team	Medium	Leader/team member profiles
cards-link	Low	Quick link lists

Interactive Blocks (8)

Block Name	Complexity	Notes
accordion	Medium	Product listings with expandable content
tabs	Medium	Content organization
carousel	High	Image/content slider
video	Medium	Inline video player
video-modal	High	Lightbox video player
search	High	Site search with filtering
filter	High	Pipeline/content filtering
modal	Medium	Popup dialogs

Content Blocks (8)

Block Name	Complexity	Notes
columns	Low	Multi-column layouts
quote	Low	Testimonials, pull quotes
table	Medium	Data tables
pipeline-table	High	Interactive drug pipeline
embed	Medium	External content
download	Low	PDF/document links
cta-banner	Medium	Full-width call-to-action
divider	Low	Section separators

Form Blocks (3)

Block Name	Complexity	Notes
form	High	Contact forms
newsletter	Medium	Email signup
search-input	Medium	Search box

3.2 Block Summary

Category	Block Count	Avg Complexity
Navigation	3	Medium
Hero	5	Medium-High
Cards	8	Medium
Interactive	8	High
Content	8	Medium
Forms	3	Medium-High
Total	35	Medium-High

4. Technical Requirements

4.1 Design System

Typography

Font	Usage	Source
F37 Lineca	Headlines, display	Custom (licensing required)
Roboto	Body text	Google Fonts

Color Palette

Color	Hex	Usage
AbbVie Blue	#071D49	Primary brand
Light Blue	#0071CE	Accent, links
White	#FFFFFF	Backgrounds
Gray	#F5F5F5	Secondary backgrounds
Dark Gray	#333333	Body text

4.2 Integrations Required

Integration	Priority	Complexity
Adobe Analytics	High	Medium
Video hosting (existing)	High	Low
Search (Algolia/similar)	Medium	High
News feed API	Medium	Medium
Careers redirect	Low	Low
Investor site links	Low	Low

4.3 Performance Targets

Metric	Target	Current Benchmark
LCP	< 2.5s	TBD
FID	< 100ms	TBD
CLS	< 0.1	TBD
Lighthouse Score	> 90	TBD
Page Weight	< 1MB	TBD

5. Resource Requirements

5.1 Team Structure

Role	Count	Responsibilities
Project Manager	1	Timeline, coordination, stakeholder management
Technical Lead	1	Architecture, code review, technical decisions
EDS Developer	2-3	Block development, JavaScript, CSS
Content Strategist	1	Content mapping, information architecture
Content Author	1-2	Content migration, markdown authoring
QA Engineer	1	Testing, validation, accessibility
Total	7-9	

5.2 Skills Required

Skill	Level	Team Members
Adobe Edge Delivery Services	Expert	Tech Lead, Developers
JavaScript/CSS	Advanced	Developers
AEM/Universal Editor	Intermediate	All
Content authoring	Intermediate	Content team
Accessibility (WCAG)	Advanced	QA, Developers
Git/GitHub	Intermediate	All


5.3 External Dependencies

Dependency	Owner	Risk Level
Font licensing (F37 Lineca)	AbbVie	Medium
Video hosting access	AbbVie	Low
Analytics configuration	AbbVie	Medium
Domain/DNS changes	AbbVie IT	High
Content approvals	AbbVie Marketing	High
Legal/Compliance review	AbbVie Legal	High

6. Timeline & Phases

6.1 Gantt Chart

ABBVIE.COM EDS MIGRATION - PROJECT GANTT CHART (18 Weeks)

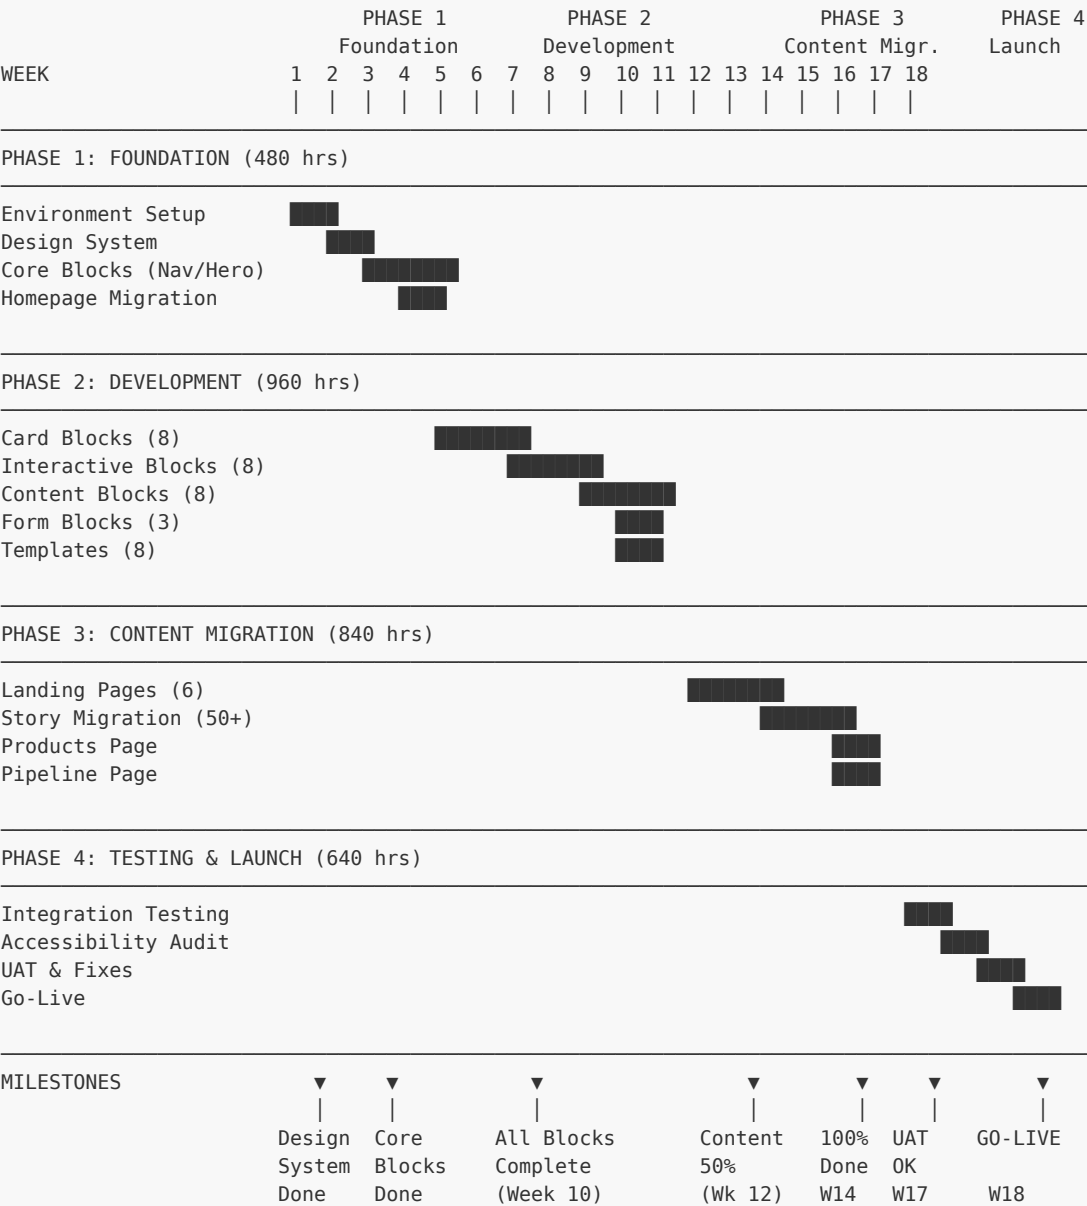

LEGEND: = Active Work Period ▼ = Milestone
Total: 2,920 Hours | 18 Weeks | 7-9 FTEs | ~\$560K

6.2 Phase Overview

Phase 1: Foundation (Weeks 1-4) ————— 480 hours

- └─ Project setup & planning (80 hrs)
- └─ Design system extraction (120 hrs)
- └─ Core block development (200 hrs)
- └─ Homepage migration (80 hrs)

Phase 2: Core Development (Weeks 5-10) ————— 960 hours

- └─ Block development - Cards (160 hrs)
- └─ Block development - Interactive (280 hrs)
- └─ Block development - Content/Forms (200 hrs)
- └─ Template creation (160 hrs)
- └─ Section landing pages (160 hrs)

Phase 3: Content Migration (Weeks 11-14) ————— 640 hours

- └─ Static page migration (200 hrs)
- └─ Story/article migration (160 hrs)
- └─ Product data migration (120 hrs)
- └─ Pipeline implementation (160 hrs)

Phase 4: Testing & Launch (Weeks 15-18) ————— 480 hours

- └─ Integration testing (120 hrs)
- └─ Performance optimization (80 hrs)
- └─ Accessibility audit & fixes (120 hrs)
- └─ UAT & stakeholder review (80 hrs)
- └─ Go-live preparation (80 hrs)

TOTAL PROJECT HOURS: 2,560 hours

6.3 Detailed Timeline by Week

Phase	Week	Activities	Hours	Deliverables
Phase 1	1	Project kickoff, environment setup, stakeholder alignment	120	GitHub repo, AEM setup, RACI matrix
	2	Design token extraction, typography setup, color system	120	styles.css, fonts.css, design tokens
	3	Header block, footer block, navigation structure	120	header/, footer/, nav.md
	4	Hero blocks (5 variants), homepage migration	120	hero-*, homepage.md
Phase 2	5	Card blocks (cards, cards-story, cards-stats, cards-feature)	160	4 card block variants
	6	Card blocks (cards-cta, cards-news, cards-team, cards-link)	160	4 card block variants
	7	Interactive blocks (accordion, tabs, carousel)	160	3 interactive blocks
	8	Interactive blocks (video, video-modal, search, filter)	160	4 interactive blocks
	9	Content blocks (columns, quote, table, pipeline-table)	160	4 content blocks
	10	Content blocks (embed, download, cta-banner), forms, templates	160	3 blocks + forms + templates
Phase 3	11	Section landing pages (Who We Are, Science, Patients)	160	3 landing pages + sub-pages
	12	Section landing pages (Join Us, Sustainability, Utility)	160	3 landing pages + sub-pages
	13	Story/article migration (25 stories), content hub setup	160	25+ story pages
	14	Product page (150+ accordions), pipeline page, remaining stories	160	Products, Pipeline, 25+ stories
Phase 4	15	Integration testing, cross-browser testing, mobile testing	120	Test reports, bug fixes
	16	Accessibility audit (WCAG 2.1 AA), performance optimization	120	A11y report, LCP optimization
	17	UAT with stakeholders, content review, final fixes	120	UAT sign-off
	18	DNS cutover prep, go-live, post-launch monitoring	120	Production site live

6.4 Hours by Role per Phase

Role	Phase 1	Phase 2	Phase 3	Phase 4	Total Hours
Project Manager	60	80	60	80	280
Technical Lead	100	160	80	100	440
EDS Developer 1	140	280	160	100	680
EDS Developer 2	100	280	160	60	600
EDS Developer 3 (50%)	40	80	60	40	220
Content Strategist	40	40	40	20	140
Content Author 1	0	40	160	40	240
Content Author 2 (50%)	0	0	120	0	120
QA Engineer	0	0	0	200	200
Phase Totals	480	960	840	640	2,920

6.5 Milestones

Milestone	Target Week	Hours to Date	Dependencies	Exit Criteria
Environment Ready	Week 1	120	AEM access, GitHub	Repo created, local dev working
Design System Complete	Week 2	240	Font licensing	All tokens in CSS, typography ready
Core Blocks Complete	Week 4	480	Design approval	Header, footer, 5 hero variants
All Blocks Complete	Week 10	1,440	Dev capacity	35 blocks tested and documented
Content Migration 50%	Week 12	1,760	Content availability	Landing pages + 25 stories
Content Migration 100%	Week 14	2,080	Content approval	All 100 pages migrated
UAT Sign-off	Week 17	2,320	Stakeholder time	All critical issues resolved
Go-Live	Week 18	2,560	DNS, legal approval	Production site live

6.6 Critical Path

Week 1-2: Environment + Design System (CRITICAL - blocks dependencies)
↓
Week 3-4: Header/Footer + Hero (CRITICAL - all pages need these)
↓
Week 5-10: Block Development (parallel tracks possible)
↓
Week 11-14: Content Migration (depends on all blocks)
↓
Week 15-17: Testing + UAT (depends on content complete)
↓
Week 18: Go-Live (depends on UAT sign-off)

Critical Path Items:

- 1. Font licensing must be resolved by Week 1
- 2. Header/Footer blocks gate all page development
- 3. Pipeline-table block is highest complexity - start Week 7
- 4. Content approvals needed by Week 10 for migration
- 5. DNS changes must be scheduled 2 weeks before go-live

7. Cost Estimation

7.1 Labor Costs - Detailed Breakdown

By Role

Role	Rate/Hr	Hours	Total	Notes
Project Manager	\$150	280	\$42,000	Planning, coordination, reporting
Technical Lead	\$200	440	\$88,000	Architecture, code review, decisions
EDS Developer 1 (Senior)	\$185	680	\$125,800	Core blocks, complex components
EDS Developer 2 (Mid)	\$165	600	\$99,000	Standard blocks, templates
EDS Developer 3 (Junior, 50%)	\$140	220	\$30,800	Support, simple blocks
Content Strategist	\$135	140	\$18,900	IA, content mapping
Content Author 1	\$95	240	\$22,800	Primary content migration
Content Author 2 (50%)	\$95	120	\$11,400	Secondary migration support
QA Engineer	\$130	200	\$26,000	Testing, accessibility
Subtotal Labor		2,920	\$464,700	

By Phase

Phase	Hours	Labor Cost	% of Total
Phase 1: Foundation	480	\$82,000	18%
Phase 2: Development	960	\$168,000	36%
Phase 3: Content Migration	840	\$122,000	26%
Phase 4: Testing & Launch	640	\$92,700	20%
Total	2,920	\$464,700	100%

By Activity Type

Activity	Hours	Cost	Description
Project Management	280	\$42,000	Planning, status, coordination
Architecture & Design	200	\$40,000	System design, technical decisions
Block Development	1,200	\$204,000	35 blocks (avg 34 hrs/block)
Template Development	160	\$27,200	8 page templates
Content Migration	520	\$49,400	100 pages (avg 5 hrs/page)
Integration Work	160	\$27,200	Analytics, search, APIs
Testing & QA	320	\$48,000	Functional, accessibility, UAT
Documentation	80	\$12,800	Technical docs, runbooks
Total	2,920	\$464,700	

7.2 Block Development Hours Detail

Block Category	Count	Avg Hrs/Block	Total Hours	Cost
Navigation (header, footer, breadcrumb)	3	50	150	\$27,000
Hero variants	5	30	150	\$27,000
Card variants	8	25	200	\$36,000
Interactive (accordion, tabs, carousel, etc.)	8	45	360	\$64,800
Content blocks	8	25	200	\$36,000
Form blocks	3	40	120	\$21,600
Total Blocks	35	34 avg	1,180	\$212,400

Note: Hours include development, styling, testing, and documentation per block

7.3 Additional Costs

Item	Cost	Frequency	Annual Cost	Notes
Adobe EDS Licensing	TBD	Annual	TBD	Per Adobe enterprise agreement
Font Licensing (F37 Lineca)	\$8,000	One-time	\$8,000	Web font license for enterprise
Search Service (Algolia)	\$600/mo	Monthly	\$7,200	If implementing site search
Image CDN (optional)	\$200/mo	Monthly	\$2,400	If using external image optimization
SSL Certificate	Included	-	\$0	Included with EDS
Subtotal Additional			\$17,600	First year

7.4 Contingency & Risk Buffer

Contingency Type	Base Amount	%	Buffer Amount
Scope contingency	\$464,700	10%	\$46,470
Technical risk buffer	\$212,400	15%	\$31,860
Schedule buffer	-	2 weeks	Included in timeline
Total Contingency			\$78,330

7.5 Total Cost Summary

Category	Amount
Labor (2,920 hours)	\$464,700
Additional Costs (Year 1)	\$17,600
Contingency (15%)	\$78,330
Project Total	\$560,630

Cost Range Scenarios

Scenario	Hours	Cost	Notes
Optimistic	2,400	\$425,000	No major issues, experienced team
Expected	2,920	\$560,000	Planned estimate with contingency
Conservative	3,500	\$675,000	Complex issues, scope additions

Note: Estimates based on blended agency rates. Internal team costs may vary significantly.

8. Risk Assessment

8.1 Risk Matrix

Risk	Probability	Impact	Mitigation
Content approval delays	High	High	Early stakeholder engagement, phased reviews
Complex interactive components	Medium	High	Technical spike early, fallback options
Font licensing issues	Medium	Medium	Identify alternatives early
Scope creep	High	Medium	Strict change control process
Resource availability	Medium	Medium	Cross-training, backup resources
Performance issues	Low	High	Early performance testing
Third-party integrations	Medium	Medium	Integration testing phase
Accessibility compliance	Medium	High	WCAG audits throughout

8.2 Key Assumptions

- AbbVie provides timely content approvals
- Existing video hosting remains accessible
- No major redesign required (visual refresh acceptable)
- Analytics configuration provided by AbbVie
- Legal/compliance review integrated into timeline
- No internationalization required in initial scope

9. Success Criteria

9.1 Technical Success Metrics

Metric	Target
Lighthouse Performance	> 90
Lighthouse Accessibility	> 95
Lighthouse SEO	> 95
Core Web Vitals (all)	Pass
Cross-browser compatibility	Chrome, Safari, Firefox, Edge
Mobile responsiveness	100% pages

9.2 Business Success Metrics

Metric	Target
Page load time improvement	> 30%
Content authoring time	< 50% of current
Time to publish	< 5 minutes
Uptime SLA	99.9%

10. Appendices

Appendix A: Current Site Technical Stack

- **Platform:** Adobe Experience Manager (AEM)
- **CDN:** Akamai (assumed)
- **Analytics:** Adobe Analytics
- **Video:** Custom/third-party hosting
- **Forms:** AEM Forms
- **Search:** Custom implementation

Appendix B: Page URL Inventory

See attached spreadsheet for complete URL inventory.

Appendix C: Block Component Specifications

Detailed specifications to be developed during Phase 1.

Appendix D: Content Migration Mapping

Content-to-template mapping to be developed during discovery.

Document History

Version	Date	Author	Changes
1.0	Feb 2026	Migration Team	Initial document

This migration plan is a living document and will be updated as the project progresses.
